



City of Patterson  
 Department of Engineering  
 1 Plaza  
 P.O. Box 667  
 Patterson, CA 95363  
 Phone (209) 895-8060 Fax (209) 895-8069

City Name: City of Patterson

---

Project Name: Las Palmas Avenue Overlay 2018-C-007

---

Date: 1/15/2026

---

Revenue		Expenses	
City Funds	100,000	Project Budget	1,501,783
Federal Funds-STBGP	286,998	Encumbered	
State Funds		Expended: Measure L	543,534
Measure L Funds	611,794	Expended: Other	923,757
Other Funds-Cal Recycle Grant	36,425		
Other Funds-SB1	466,567	To be transferred out	34,492
<b>Total</b>	<b>1,501,783</b>		

Revenue and Expense include all aspects of the project that use Measure L Funds. Design, construction management and Construction all included. Expenses shown include all to date as of 10/14/24.

Completion Date: Construction Completed December 2021. Closeout Paperwork was Submitted.

---

Phase: Project Complete

---

**Overall Project Details:**

---

This project consisted of pavement overlay incorporated with recycled asphalt. The project site is located along Las Palmas Avenue from Ward Avenue to the east end of the City limit in the Patterson, California. The road segment where construction occurred spans approximately 1.25 mile. Prior to overlaying, pavement surfaces with severe conditions were excavated and reconstructed with aggregate base and asphalt concrete. The existing road was cold planed where it ties into the existing road sections and along existing gutter sections. All existing striping, markings, and markers were removed in preparation for the overlay and disposed of in accordance with regulations, and replaced with thermoplastic striping, markings, and reflective markers. Existing manholes and valve covers were raised to the final grade. Additionally, all crosswalks within the project area were reconstructed to meet the most current Americans with Disabilities Act (ADA) Standards. This was done in an effort to maintain and improve roadway safety within the City of Patterson.

The design phase of this project has been completed. The project went out to bid on Thursday, December 17, 2020, and the contract was awarded by City Council on February 2, 2021. Construction started March of 2021 and was completed December 2021. The Project was taken to City Council March 15, 2022 for completion. Final closeout paperwork was submitted in June of 2022. Project is complete.

**Project Status:**

**Design Phase**


Proposal Due: February 19, 2019  
 Consultant Selection: May 8, 2019  
 City Council Approval: May 21, 2019  
 Design Contract Executed: July 7, 2019  
 Design Complete: June 2020

**Construction Phase**

Bids Due: December 17, 2020  
 Contractor Selection: December 21, 2020  
 City Council Approval: February 2, 2021  
 Contract Executed: February 11, 2021

Construction Completed: December-21  
 Project Completion: March 15, 2022

**Add photos/renderings:**

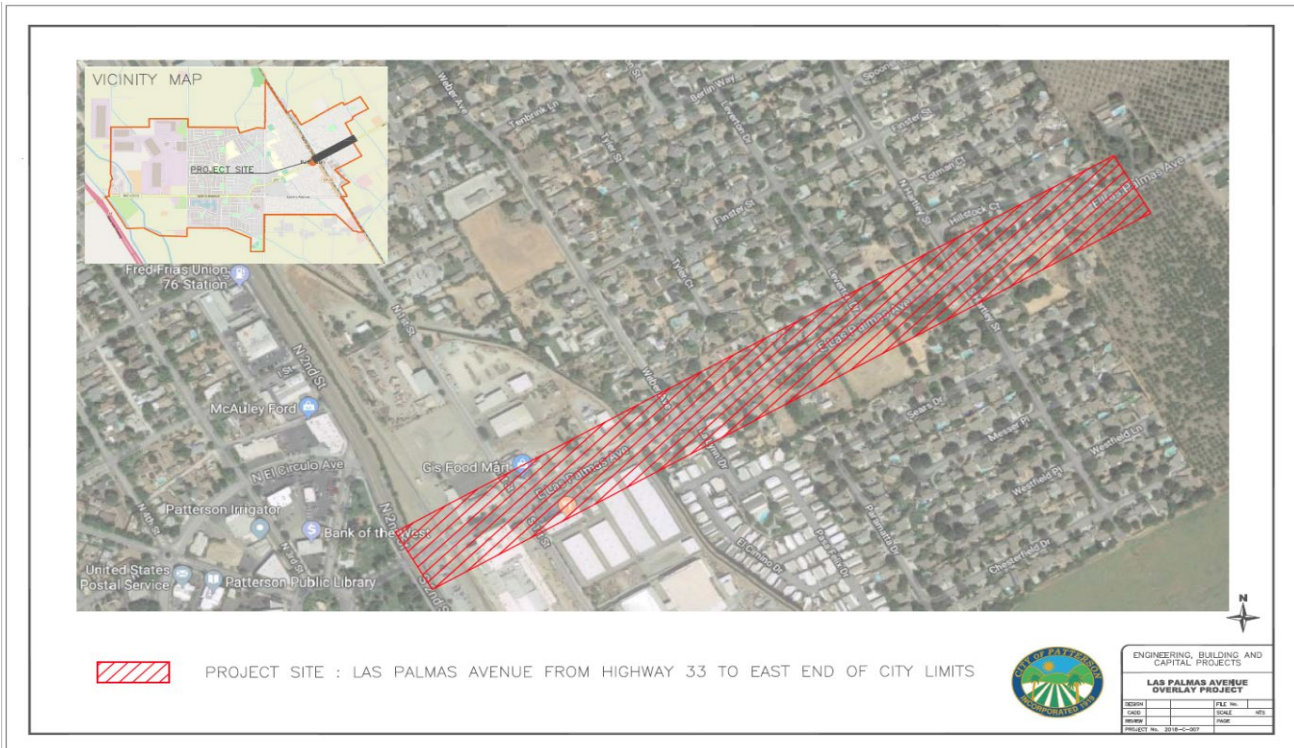

Measure L Funding Sign in Place



Paving at Las Palmas Avenue and First Street

