



City of Patterson  
Department of Engineering  
1 Plaza  
P.O. Box 667  
Patterson, CA 95363  
Phone (209) 895-8060 Fax (209) 895-8069

## Measure L

---

City Name: City of Patterson

---

Project Name: Ward Avenue Improvements - Phase 2 2023-C-010

---

Date: 1/15/2026

---

Revenue		Expenses	
City Funds		Project Budget	93,111
Federal Funds		Encumbered	
State Funds		Expended - Measure L	61,638
Measure L Funds	93,111	Expended - Other	-
Other Funds			
<b>Total</b>	<b>93,111</b>	Available	<b>31,473</b>

Revenue and Expense include all aspects of the project that use Measure L Funds. Expenses are current as of July 2025. Only design contract utilizes Measure L.

### Estimated

Completion Date : January 20, 2026

---

Phase: Construction

---

### Overall Project Details:

---

Currently, Ward Avenue is one of the City's busiest streets. Ward Avenue is a north/south two lane collector roadway. It serves the surrounding residential neighborhoods as a main roadway to their destinations. There are several schools located in the vicinity causing heavier traffic volumes in the mornings and afternoons. There are residential homes that back up to this portion of Ward Avenue with downtown being just east of the project area.

This project consists of providing a 2-inch overlay on Ward Avenue from West Las Palmas to North 9th Street. Prior to overlaying, badly damaged pavement areas will be excavated and reconstructed with aggregate base and asphalt concrete. The existing road will be cold planed where tying into the existing road sections and along existing gutter sections prior to the overlay. Upon completion of the overlay, existing manhole and valve covers will be raised and thermoplastic striping and pavement markings applied.

**Project Status:**

---


A request for proposals for design services was prepared and advertised in August 2023. Proposals were evaluated with Provost and Pritchard rated the highest. After successful negotiations between the City and Provost, the design contract was awarded on November 7, 2023 at the City Council Meeting. The design phase of this project has been completed, and the project is out to bid for construction. The project was put out to bid in June 2024, but unfortunately, only one bid was received. Since the project is funded with federal funds for the construction phase, Caltrans LAPM requires the City to analyze and justify the single bid if only one is submitted. After discussions with two contractors, it was found that the Valley Builders Exchange did not advertise the project in time for contractors to bid. As a result, the City rejected the sole bid at the August 20, 2024 City Council meeting and decided to re-advertise the project. The re-bid opened on November 6, 2024, and the City received 10 bids. The contract was awarded to Platinum Dirt Worx, LLC at the January 21, 2025 City Council meeting. Construction started the second week of April, a final walk was performed on May 29, 2025. The project is near completion pending some punchlist items. The project is scheduled to be accepted as complete January 20, 2026.

---

**Notes:** Please note that the report for Quarter 1 was understated by \$3,359.40.  
That amount has been added to Quarter 2 to correct the variance.

Add photos/renderings:

## ATTACHMENT A - PROJECT LOCATION MAP

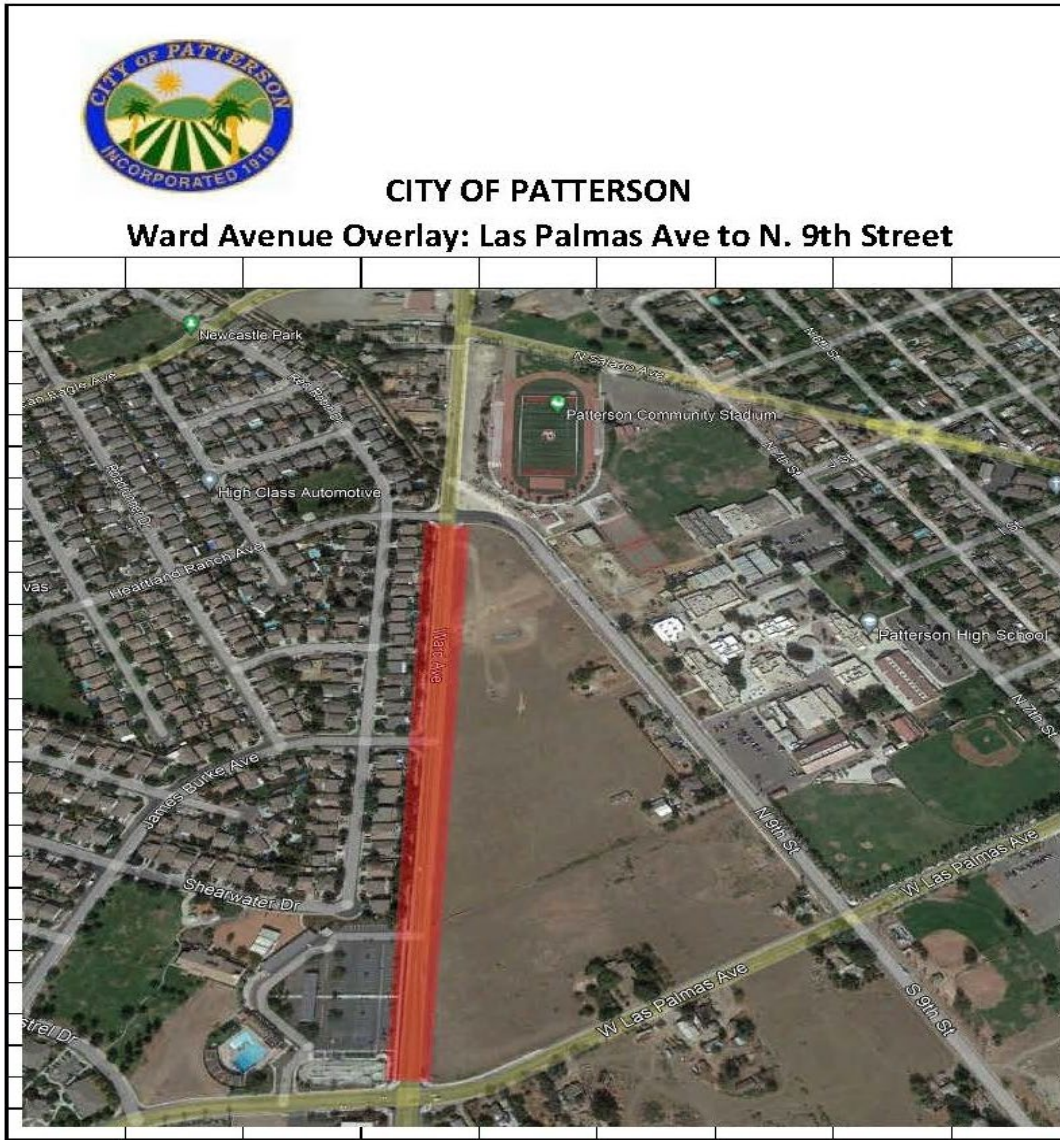

Project Limits: Ward Avenue from  
Las Palmas Ave to N. 9th Street



After



May 29, 2025 at 10:41:40 AM  
+37.471321,-121.140923  
Patterson, CA

